

Tempus Resource

Quick Reference Guide

Project Manager & Service Manager (PM/SM, Blended PM/SM + PPM)

Knauf · Phase 1 · Planner Onboarding

Note: This guide focuses on the day-to-day Planner workflow for PM and SM (and Blended PM/SM + PPM). Resource Managers (RM) and Bulk Project Allocation are out of scope for this release and will be covered in a separate guide.

Contents

Right-click here and choose 'Update Field' (or press F9) to build the table of contents.

How to Use This Guide

PM/SM

Blended PM/SM + PPM

This guide is built for **Planners** at Knauf — Project Managers (PM), Service Managers (SM), and the Blended role (PM/SM + PPM). It walks you through the two workflows you will use every day:

1. **Create a project** — set it up so that the right people, dates and money land in Tempus from day one.
2. **Find an existing project and edit it** — the same set of pages, just in update mode.

Every workflow ends in the same three pillars. Master them once, and the rest is repetition:

Pillar	What it answers	Where you do it
Attributes	<i>What</i> is this project? (Owner, Phase, Business Unit, Dates, Tags ...)	Attributes page
Resources	<i>Who</i> and <i>how much</i> ? (named people, generic demand, time grain)	Single Project Allocation grid
Financials	<i>What does it cost</i> ? (Hourly Rate, Cost Plan, Budget, Actuals)	Financials page

Tip: Whenever a step says "do the same thing later when editing", you can jump straight to the relevant pillar chapter — chapters 5–7 are written so they work for both Create and Edit.

Roles in This Guide

Role	What you will plan	In this guide
PM — Project Manager	Standard projects (Intake → Active → Closed)	Full scope
SM — Service Manager	Services / non-project activities (Run, Admin, Change)	Full scope; "Service" vs. "Project" differences flagged inline
Blended PM/SM + PPM	Both, plus Portfolio overview	Full scope; PPM cross-references at end of each chapter

Out of scope here: **Resource Manager (RM)** workflows (Bulk Project Allocation, Resource Replace, Heatmap administration). A dedicated RM guide will follow.

Valkeen GmbH · Bahnhofstrasse 64 · 8001 Zurich, Switzerland
www.valkeen.com · © 2026 Valkeen GmbH. All rights reserved.

Time Grain Defaults — set these once

Time grain and capacity unit are the two settings that change how every grid in Tempus looks. The Knauf defaults are:

Setting	Knauf default	Where to change
Time granularity	Month	SPA grid → ribbon above the timeframe
Capacity unit	Hours (PM/SM views also show Mandays)	SPA grid → ribbon above the timeframe
Working hours / day	8 h	Configured globally (admin-only)
Working hours / month	~168 h (varies per German public-holiday calendar)	Configured globally (admin-only)

Note: If you change time grain or capacity unit on the SPA grid, the change is **per view, per user** — it does not affect anyone else.

Sign-in and Homescreen

Logging in

Tempus Resource is reached via the Knauf Tempus instance at `knaufdev.tempus-resource.com` (DEV) or the production URL once go-live is finalised.


How to

1. Open **Google Chrome** (recommended browser).
2. Navigate to the Tempus URL provided by your Knauf admin.
3. Click **Knauf SSO Login** — you will be redirected to the Knauf identity provider.
4. Enter your standard Knauf credentials. Multi-factor follows the standard Knauf policy.
5. You land on the Tempus **Homescreen**.

Note: If the SSO redirect fails, click *Or use other methods* and request a local fallback from the Tempus admin. PM/SM do not have shared accounts — each Planner signs in with their own identity, which also drives the "my projects" filter on the grid.

PM/SM Homescreen

After login you land on a focused Homescreen. PM/SM see two main tiles plus the standard top bar:



PM/SM Homescreen with two tiles

At a glance

- **Project Management** tile — opens the Project Management Grid (your starting point for "find a project").
- The + badge on the tile opens the **Create Project** dialog directly without going through the grid first (see chapter 4).
- **Report Management** tile — opens your subscribed and saved reports.
- **Top bar** with global search, notifications, help, the hamburger menu and your profile.

Note: If your Knauf account also carries the PPM role, you may see an additional **Portfolio Overview** tile. RM tiles (Resource Management, Bulk Project Allocation Flatgrid, All Resources) are intentionally hidden for the PM/SM scope of this guide.

Top Bar Reference

The blue top bar is identical on every screen in Tempus. Each icon is a single click.

Valkeen GmbH · Bahnhofstrasse 64 · 8001 Zurich, Switzerland
www.valkeen.com · © 2026 Valkeen GmbH. All rights reserved.

Element	What it does	Tip
Tempus logo (left)	Returns to the Homescreen from anywhere	Single click — no confirmation
Global Search	Searches across Projects, Resources, Attributes and Reports	Use a contains logic, narrow with the filter checkboxes
Bell — Notifications	Shows pending Resource Requests and system alerts	Red dot = unread count
Help (?)	Opens the in-app help and the Knowledge Base	Knauf admin can pin custom topics
Hamburger ☰	Full navigation menu (alternative to the homescreen tiles)	Useful when you are deep inside a project
Profile (right)	Your account, language and sign-out	Language defaults to English for Knauf

Notification Subscriptions

Notifications keep you in the loop for the few moments where you actually need to react:

How to

1. Click the **bell** in the top bar.
2. Choose **Manage subscriptions**.
3. Subscribe to the events that matter for your role — typically: *Resource Request approved/rejected*, *Project status changed*, *Attribute value changed for my projects*.
4. Pick the delivery channel (in-app, email, or both). Knauf default: in-app + email digest.
5. Save. New events appear in the bell drop-down within seconds.

Tip: Don't subscribe to "all changes on all projects" — the noise will bury the important ones. Start with *Resource Request* events and add the rest only if you actually miss something.

Create a Project

PM/SM

Blended PM/SM + PPM

Creating a project is the entry point for every Planner workflow. At Knauf there are two starting points, depending on whether the project has been pre-approved through the Intake process or whether the PMO wants to seed a brand-new project shell. Both lead to the same three pillars (Attributes → Resources → Financials), which are covered in chapters 5–7.

At a glance

- Two ways to create a project at Knauf:
- **Without a template** — typed straight into Tempus; used for quick service-style work and ad-hoc demand.
- **With a template** — used when an Intake item has already been approved, or when the PMO wants the project to start from a baseline shell (status set, attributes pre-filled, owner assigned).

Where to start a project

PM/SM can open the **Create Project** dialog from three different entry points — pick whichever is closer to where you currently are in the tool:

Entry point	When to use it
+ badge on the <i>Project Management</i> tile (Homescreen)	You just logged in and have nothing else open
+ Add projects button in the Project Management Grid toolbar	You are already browsing the grid
Intake screen → Approve & Create	The project came in through Intake and is now being formalised

Tempus™ Resource

Project name **Create** Attributes

Intake Form

- Type * Project
- Service Name * Project - n.a.
- Division * Not set
- Product/ Platform Area * Not set
- Lead Product/Platform * Not set
- Business Portfolio * Not set
- Planned Start date 01.01.2027
- Planned End Date 31.12.2027
- Program Not Set
- Categorization Not Set
- Project Category Not Set
- Project Charging Type * Not set
- Legal Entity *
- Program Evolution Relation * Not set
- Project Manager Not Set

PMO

- Above Red Line Not Set
- Portfolio Status 0 - Draft

Create Project dialog (Intake)

Path A — Create *without* a template

Use this path for services, BAU work and any project where you do **not** want to inherit predefined attributes or assignments.

How to

1. From the Homescreen, click the + on the *Project Management* tile (or + **Add projects** in the grid).
2. In the dialog, choose **Create blank project** (no template selection).
3. Enter the **Project name**. Knauf naming convention: <Project type abbreviation> – <short scope>, e.g. BAU – AD Hardening 2026.
4. Set the **Start date** and **End date**. These must be valid before the Single Project Allocation grid will accept assignments.

5. Confirm with **Create**. Tempus opens the new project's **Attributes** page automatically.

6. Continue with chapter 5 — *Set up Attributes* — to fill the mandatory master data before moving to Resources and Financials.

Note: A blank-project shell is created in status Intake / Draft until the mandatory attributes (chapter 5) are filled. You can save and come back, but the project will not show up in dashboards until status is moved to Active and the owner is assigned.

Path B — Create *with a template* (PMO project)

Use this path when an Intake item has been approved by the Knauf PMO, or when a standard project profile applies (e.g. "Knauf IT Standard Project").

Division *	Not set	Product/ Platform Area *	Not set
Lead Product/Platform *	Not set		
Business Portfolio *	Not set		
Planned Start date	01.01.2027	Planned End Date	31.12.2027
Program	Not Set		
Categorization	Not Set		
Project Category	Not Set		
Project Charging Type *	Not set		
Legal Entity *			
Program Evolution Relation *	Not set		
Project Manager	Not Set		

PMO

Above Red Line	Not Set
Portfolio Status	0 - Draft
Ranking	Not Set
Ext. Project Number	UNIQUE
Project Identifier Code(WBS)	

10.1.1 2026 ProSymmetry LLC. All rights reserved.

Create Project from PMO template

How to

1. From the Homescreen, open **Project Management** and click **+ Add projects → Create from template**.
2. Pick the relevant template — the Knauf default templates are listed alphabetically, prefixed with TPL_.
3. The dialog pre-fills:
4. Project status (Active or Planning, depending on template)
5. Default attribute values (Business Unit, Phase, Cost Center, ...)
6. A predefined task structure on the Allocation grid (e.g. "Specification / Build / Test / Hypercare")
7. Override **Project name**, **Start/End date**, and **Project owner** as needed — these are the four fields that are almost always template-specific.
8. Click **Create**. Tempus opens the new project on the Attributes page.
9. Walk through chapters 5–7 once to validate the inherited values; in 80 % of cases you only adjust **dates** and **owner**.

Note: Tip — bulk-fill: If you create several similar projects in a row (typical at the start of a fiscal year), use the **Clone** action on an existing project from the grid instead of going through the template dialog every time.

What happens after Create

On a successful Create, Tempus drops you straight onto the new project's **Attributes** page. From here the path is always the same:

1. **Attributes** — fill the master-data fields (chapter 5).
2. **Resources** — open the Single Project Allocation grid and add the planned demand (chapter 6).
3. **Financials** — set the rate card, the Cost Plan, and the Budget (chapter 7).
4. **Save & Check-in** — release your check-out so other Planners can edit, and the figures appear in dashboards (covered at the end of chapter 6).

Warning: Until you **save and check in**, the project is invisible to RM Resource Requests and to Reports. A brand-new project that is never checked in will sit silently in your drafts without any visibility.

Pillar 1 — Attributes (Master Data)

PM/SM

Blended PM/SM + PPM

Attributes describe **what** the project is. Every report, every dashboard tile and every Resource Request inherits from attributes — incorrect master data here makes the rest of the tool unreliable.

This chapter applies to both moments:

- When you have **just created** a project (chapter 4 → continue here).
- When you have **opened an existing** project and need to update master data (chapter 8 → comes back here).

The page itself, the fields, the edit-loop and the validation are identical.

The Attributes page at a glance

After Create, Tempus opens the project shell with the **Attributes** tab active. The layout has three zones:

Tempus™ Resource

PROJECT NAME: **Service CRM** **Save**

CREATED 04.05.2026 MG Magdalena Gint... UPDATED 08.05.2026 MG Magdalena Gint...

Intake Form

- Type * Service
- Division * Enterprise Solu...
- Lead Product/Platform * SFX Platform
- Business Portfolio * MoB
- Planned Start date 01.01.2027
- Planned End Date 31.12.2027
- Program Not Set
- Categorization existing
- Project Category Maintenance
- Project Charging Type * Not set
- Legal Entity *
- Program Evolution Relation * beneficial
- Project Manager Marco Hessefort

PMO

- Above Red Line Not Set

Attributes page layout

At a glance

- **Top — Project header** with project name, status pill, project owner, start/end dates and the **Check-out / Check-in** button.
- **Left — Attribute groups** ("General", "Classification", "Time & Money", "Custom" — Knauf-specific group labels may differ slightly per template).
- **Centre — Attribute fields**, grouped by the section selected on the left. Required fields are marked with a small red asterisk.
- **Right — Audit & Activity** column (recent changes, last edited by, version pin).

Note: Check-out is **automatic** as soon as you start editing an attribute, provided no one else holds the lock.

The header switches from a green *Available* pill to a yellow *Checked out by you* pill.

What to maintain at create time

The Knauf go-live scope expects PM/SM to populate these fields on every new project. Templates pre-fill many of them, but always verify.

Group	Field	Why it matters	PM/SM-fillable?
General	Project name	Identifies the project everywhere	Yes
General	Project type	Standard / Service / BAU / Non-project (Admin, Run ...)	Yes (limited list)
General	Status	Drives visibility on the grid and in reports	Yes — see status flow below
General	Project owner	Default Planner used in Quick Filters	Yes
Classification	Business unit	Cost-center alignment	Yes
Classification	Phase	Drives template lifecycle (Intake → Planning → Active → Hypercare → Closed)	Yes
Time & Money	Start / End date	Boundaries of the SPA grid	Yes
Time & Money	Currency	EUR by default at Knauf	Read-only (admin)
Custom	Risk profile / Strategic flag / Vendor	Knauf-specific reporting	Yes

Editing rules (single project)

The page is a classic *edit-many, save-once* form — there is no per-field save, but you must trigger Save before you leave the page or the changes are dropped.

How to

1. Click into the field you want to change. Tempus auto-checks out the project on first edit (yellow pill appears in the header).

2. Make as many changes as needed across the attribute groups on the left.
3. Click **Save** in the top-right of the page.
4. Wait for the green confirmation toast in the lower-right corner. If validation fails (mandatory field missing, invalid date range, ...) the toast is red and the offending field is highlighted with a red border.
5. When all changes are saved, **Check-in** to release the lock. Other PM/SM can now edit; reports refresh on their next scheduled run.

Note: Tip — keep yourself short: the typical Knauf edit loop touches 2–3 fields (e.g. *Status*, *End date*, *Risk profile*). Don't open the page with the intent to clean all groups in one sitting; you will create more lock contention than value.

Project status flow (PM/SM-controllable)

The status field has tight rules — Tempus blocks invalid transitions with a red toast. The legal path for PM/SM:

From	To	Trigger / requirement
Draft	Active	All mandatory attributes filled; owner set
Active	On Hold	Optional, reversible
On Hold	Active	Reverses the hold
Active	Closed	End date reached AND all assignments checked out by RM
Closed	Re-open	Only by PMO admin, not PM/SM

Warning: Setting a project to *Closed* freezes the Allocation grid and the Financials page. Make sure all planned hours/costs are checked in **before** closing — there is no PM/SM bypass.

What PM/SM cannot see or edit

A few fields and pages remain RM- or admin-only at Knauf in Phase 1. They are visible on the page (grey) so you know they exist, but the field is read-only or the icon is greyed out.

Read-only for PM/SM	Owned by
---------------------	----------

Resource Rate Card overrides (per-resource)	RM / Finance
Resource Manager assignment per role	RM
Audit-log purge	Admin
Custom attribute schema changes	Admin
Lock-period setup	Finance admin

If you genuinely need one of these changed, open a **Resource Request** with comment, or contact the PMO directly.

Cross-references

- After Attributes, continue with **Resources** (chapter 6) — the same project, but now on the Allocation grid.
- For Financials (rates, Cost Plan, Budget), see chapter 7.
- To return here from the Project Management Grid later, see chapter 8 — the edit loop is identical to the one above.

Pillar 2 — Resources (Allocations)

PM/SM

Blended PM/SM + PPM

Resources answer the question **who works on this project and how much**. PM/SM at Knauf plan demand using the **Single Project Allocation (SPA) grid**. The same grid is used at create time (initial planning) and during the project lifecycle (re-planning, re-forecast).


This chapter walks through the grid layout, the standard "add a resource" loop and the most important grid options. Bulk Project Allocation (BPA) is a different grid for RM and is intentionally out of scope.

Opening the Allocation grid

From the project's Attributes page (chapter 5), switch to the Allocation grid via the **view selector** in the top-right corner of the project header (it lists *Attributes, Allocations, Financials, Audit, ...*). Pick **Allocations**.

Note: The Allocation grid only becomes editable once the project has a valid Start and End date on the Attributes page. If you forgot to set them at Create time, you will see a placeholder banner instead of the grid — go back to Attributes and fill the dates.

SPA grid at a glance

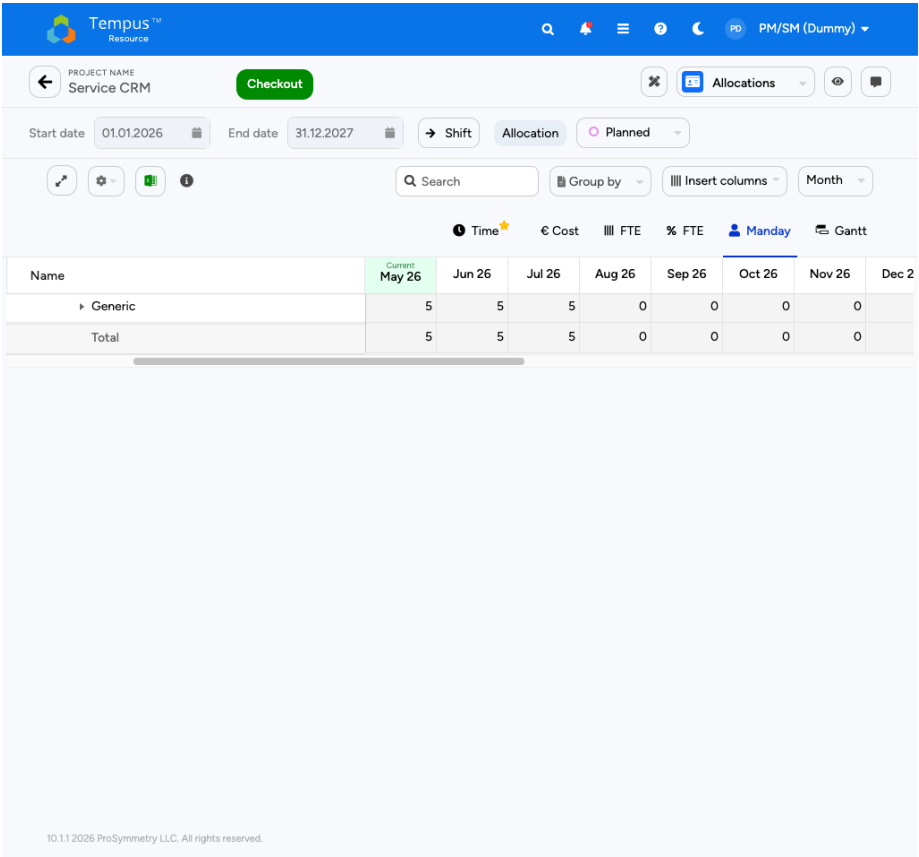

SPA grid in manday view

At a glance

- **Header strip** — project name, **Check-out** / **Check-in** button, planned status pill (PLANNED / BASELINED), Start/End date.
- **Ribbon** — main grid controls (Expand, Search, Group by, Insert columns, Time granularity, Capacity unit, Options menu).
- **Body** — rows of resources/tasks, columns of time buckets (months by default).
- **Right gutter** — totals (Total Hours, Total Mandays, FTE average, depending on capacity unit).

How to add a resource

The standard add-resource loop at Knauf:

How to

1. Click **Check-out** in the header (yellow pill appears — only you can edit).
2. Click **+ Add Row** above the grid body and pick the resource type:
3. **Named resource** — a specific person from the Resource pool. Use when you already know who will work on the project.
4. **Generic / role-based resource** — a placeholder ("Senior Dev DE", "Tester IN") that triggers a Resource Request to the RM later. Use when staffing is still open.
5. The new row appears with zeros in every time bucket.
6. Type the allocation directly into the time buckets you want to load. **Tab** moves right (next month), **Enter** moves down (next resource).
7. Repeat for additional resources.
8. Click **Save** — wait for the green toast.
9. Click **Check-in** — releases the lock. Generic rows now trigger Resource Requests automatically; named rows go into the RM's approval queue.

Note: Tip — bulk fill: select a range of cells with Shift+click, then type a value and press Enter — the value is replicated across all selected cells. Combined with **Group by Resource** this is the fastest way to load standard demand for a 12-month service project.

Ribbon options PM/SM use most

Control	What it does	Knauf default
Expand	Toggles the grid into full-screen mode	Off
Search	Searches within the grid (resource name when grouped by resource, task name when grouped by task)	Empty
Group by	Switch between <i>Resource</i> and <i>Task</i> grouping	<i>Resource</i>
Insert columns	Adds project, resource or assignment attributes as columns (Cost Center, Role, Status ...)	Role + Status
Time granularity	Month / Quarter / Year (Week is RM-	Month


only)

Capacity unit	Hours / Mandays / FTE / FTE %	Hours (PM/SM views also show Mandays)
---------------	-------------------------------	---------------------------------------

Options menu (Advanced)

Open the **Options** drop-down in the ribbon to reach the more advanced display toggles. All of them affect *only your view*, never other Planners.

Option	What it does	When to enable
Total Column	Adds a final column with the total Hours / Mandays per row	Always on at Knauf
Resource Heatmap	Background colour per cell based on overall allocation % of the resource	Useful when validating named resources against their other commitments
Resource Request Heatmap	Background colour based on Resource Request status (Pending / Approved / Rejected)	When chasing approvals before go-live of a project
Overlay Heatmap — Rows / Groups	Applies the selected heatmap to individual rows or groupings	Match the visualisation to your "Group by" choice
Tasks to show	Filters _generic vs. non-generic tasks	Hide generics during go-live freeze
Date Range Filter	Limits the grid to a sub-range without changing the project timeframe	Quarterly re-forecast loop

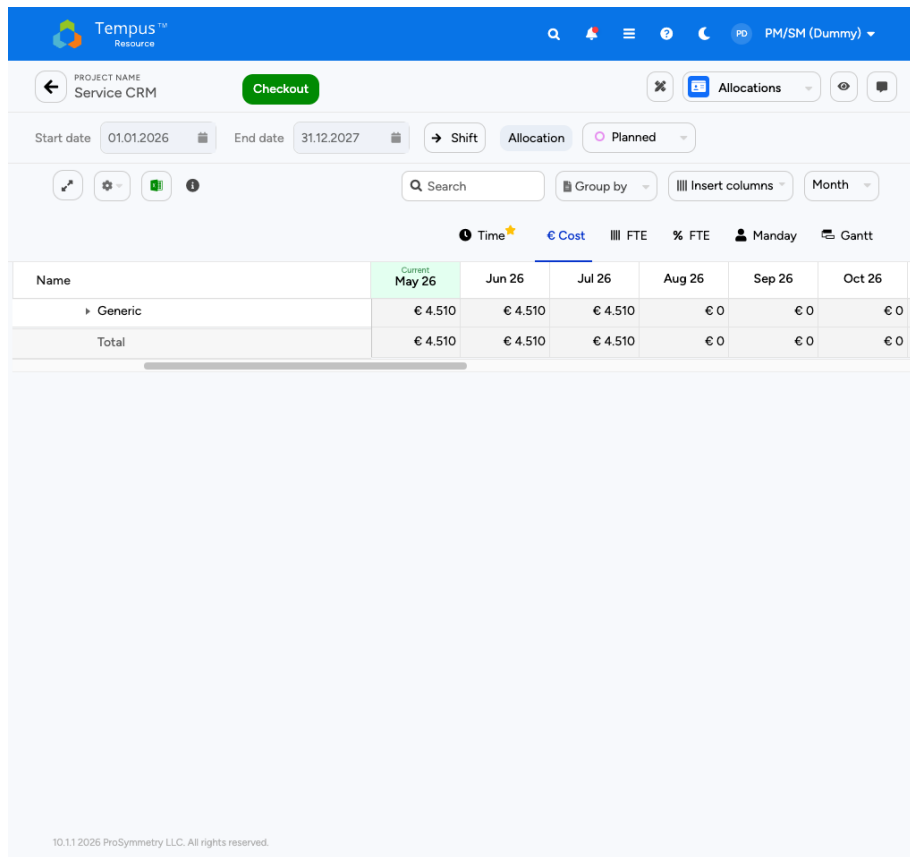

Cost view with Cost Plan overlay

Switch between Manday and Cost view

PM/SM commonly toggle between the two main views of the same SPA grid:

View	Capacity unit	Used for
Manday view	Hours or Mandays	Discussion with Project Owners, Resource Managers, status reports
Cost view	Cost (calculated from the rate card)	Discussion with Finance and PMO; cross-check against Financials page

The switch is a single click on **Capacity unit** → **Cost**; no save needed. Behind the scenes Tempus multiplies each cell's hours by the resource's Hourly Rate (chapter 7) and shows the resulting Cost.

Tip: Toggle Cost view briefly at the end of every planning session — anomalies (e.g. a senior architect accidentally loaded at junior rate) jump out immediately.

Save & Check-in — the discipline

Every change must be **saved + checked in** to be visible to the rest of Knauf:

Action	What it does	What it does NOT do
Save	Persists your edits	Does not release the lock; reports still don't see the changes
Check-in	Releases your lock; recalculates totals; triggers RM Resource Requests	Does not save unsaved edits — always Save first

Warning: A check-out left open at end of day blocks other Planners. The Knauf rule is: **always check in before lunch and before sign-off**. If you forget, an admin can force-release the lock, but you will lose unsaved edits.

Pillar 3 — Financials

PM/SM

Blended PM/SM + PPM

Financials answer **what does this project cost, and is it on budget**. At Knauf, PM/SM are accountable for the **Cost Plan** and the **Budget vs. Actual** comparison; rates and lock periods are administered by Finance / PPM but must be understood by every Planner.

This is the pillar most often skipped at Create time — and the one that pays off the most when you do it properly at the start. Plan once, re-forecast quarterly.

At a glance

- **Hourly Rate** — single value per resource (admin-maintained).
- **Advanced Rate** — time-and role-dependent rate card (admin-maintained).
- **Cost Plan** — derived from the Allocation grid × the applicable rate. PM/SM-editable for adjustments.
- **Budget vs. Actual** — Cost Plan as Plan; actual logged hours × rate as Actual.
- **Lock Periods** — closed months/quarters where Cost cannot be changed.
- **Re-forecast** — PM/SM-driven update of remaining quarters' Cost Plan.

Opening the Financials page

From the project header (Attributes, Allocations, ...), choose **Financials** in the view selector. The page shows three stacked panels:

1. Hourly Rate

The **Hourly Rate** is the simplest rate model — a single rate per resource, valid for a date range. Knauf uses it for:

- Named resources whose rate does not change with the activity (e.g. "Lina Vorontsova — Senior Architect — 145 €/h").
- Generic / role-based resources where a single blended rate is acceptable (e.g. "Senior Dev DE — 120 €/h").

PM/SM can **read** the Hourly Rate in the Rate Card panel and in any Allocation-grid column. To change it, request a rate update from Finance — there is no PM/SM-side override on the Hourly Rate.

Note: Hourly Rate is the **fallback** rate. If no Advanced Rate applies for a given month/role, Tempus uses the Hourly Rate.

2. Advanced Rate

The **Advanced Rate** is a richer rate model — multiple rates for the same resource depending on **time** (effective from / to) **and** on **role** / **activity**. Used at Knauf for:

- Annual rate uplifts (e.g. 2026 rate jumps to 150 €/h on Jan 1).
- Cross-charging where the rate depends on the role the resource is playing (Lead vs. Reviewer).
- External vendors whose rate is contract-bound and changes per phase.

Advanced Rate is administered by Finance. PM/SM see the resolved rate in the Cost view of the Allocation grid (chapter 6) and in the Cost Plan panel below.

Note: Tip — when the Cost number surprises you: open the **Insert columns** dropdown on the SPA grid and add the *Effective Rate* column. The grid will show which rate row (Hourly vs. Advanced, which date band) Tempus actually used per resource — the most common source of "wrong-cost" tickets.

3. Cost Plan

The **Cost Plan** is the financial twin of the Allocation grid. Whenever you save and check-in on the SPA grid, Tempus recalculates the Cost Plan cell-by-cell as:

``` Cost Plan[resource, month] = Hours[resource, month] × Effective Rate[resource, month] ```

For most planning sessions you do nothing here — the Cost Plan is correct because the Allocation grid is correct. The two cases where PM/SM **manually adjust** the Cost Plan:

Reason to override	Example
--------------------	---------

Fixed-price line item not driven by hours	A vendor invoice of 25 k€ in Q2, irrespective of effort
One-off cost (license, hardware)	8 k€ Tableau license in Jan
Currency adjustment manually applied	A foreign-currency external is being billed at a non-standard rate

#### How to

1. On the Financials page, in the **Cost Plan** panel, click into the target cell (resource × month).
2. Enter the override value. The cell shows a small "manual override" indicator (orange dot at the corner).
3. Click **Save** in the panel header, then **Check-in** at the project header.
4. If you need to revert to the calculated value, right-click the cell → **Reset to calculated**.

**Warning:** A manual override **survives** changes to the Allocation grid — if you later add hours to that resource/month, your override is still shown and the calculated value is hidden. Reset overrides when they no longer apply.

## 4. Budget vs. Actual

The **Budget vs. Actual** panel compares the Cost Plan (Plan) to the Actuals (logged hours × applicable rate). Three flavours are available via the panel's view selector:

View	Granularity	Used for
Monthly	One bar per month	Operational tracking
Quarterly	Q1 / Q2 / Q3 / Q4	Standard Knauf status meeting
Annual	Single Plan / Actual total	Year-end close, audit

**Note:** Actuals at Knauf are loaded from the Timesheet system once a week (Sunday night batch). A spike in Actuals on Monday morning is normal — it includes the previous week's bookings.

The **Variance** column is colour-coded:

Colour	Meaning	Knauf threshold
--------	---------	-----------------

Valkeen GmbH · Bahnhofstrasse 64 · 8001 Zurich, Switzerland  
www.valkeen.com · © 2026 Valkeen GmbH. All rights reserved.

Green	Actual within $\pm 5\%$ of Plan	OK
Amber	Variance $\pm 5\%$ to $\pm 15\%$	Flag in next status report
Red	Variance $> \pm 15\%$	Escalate to PMO; trigger re-forecast

## 5. Lock Periods

A **Lock Period** is a date range (typically a closed financial month or quarter) in which Cost cannot be changed. Lock Periods exist to protect month-end reporting from retro-active edits.

State	Symbol on the grid	What you can do
Open	No symbol	Edit freely
Soft-locked	Padlock outline	Edit with a comment (audit-tracked)
Hard-locked	Filled padlock	Read-only; no edit possible without PMO override

**Warning:** At Knauf the previous month is **soft-locked** on the 5th business day of the following month and **hard-locked** on the 10th. Schedule your Cost Plan adjustments before those dates. Soft-locked edits are tracked and reported to Finance.

## 6. Re-forecast

A **Re-forecast** is a structured update of the Cost Plan for all remaining open months/quarters of a project. The Knauf cadence is quarterly:

### How to

- 1. Trigger** — at the start of each quarter, PMO publishes the re-forecast window (typically two weeks).
- 2. Open** the project's Financials page and switch the Budget vs. Actual view to **Quarterly**.
- 3. Compare** Actuals vs. Plan for the closed quarter. Red and amber rows are your candidates for adjustment.
- 4. Adjust** the Cost Plan for the remaining quarters — preferably by editing the **Allocation grid** (chapter 6) so hours and cost stay in sync. Use manual Cost Plan overrides only for non-hour-driven items.
- 5. Save & Check-in** — the new Plan becomes the active baseline for the next quarter's reporting.

**6. Comment** — leave a short note on the Audit pane (right column) summarising what changed and why. PMO uses these comments in the quarterly variance review.

**Tip:** Don't re-forecast a project the day before status meeting — the new figures land in dashboards on the next overnight refresh, and you want the PMO to see the same Plan you discuss.

## What PM/SM cannot edit on Financials

Read-only / admin-only	Owner
Rate Card values (Hourly + Advanced)	Finance admin
Effective-date bands on the Rate Card	Finance admin
Currency configuration per project	PPM admin
Lock-period schedule	Finance admin
Actuals correction (timesheet adjustment)	Time-tracking admin

If you spot a Rate Card error or an Actual you believe is wrong, document it in the Audit pane and raise the ticket with Finance — there is no PM/SM-side workaround.

# Find and Open a Project

PM/SM

Blended PM/SM + PPM

The second daily workflow is **find an existing project and edit it**. Mechanically, the edit pages are identical to the Create-time pages you already know:

- Attributes → chapter 5
- Resources → chapter 6
- Financials → chapter 7

This chapter therefore only covers what is *different* in edit mode: the **Project Management Grid** (how to find the project) and the **Open** mechanics (how to land on the right tab the first time). For everything that happens after that, jump back to the relevant pillar chapter — the edit-loop instructions are intentionally the same.

## Project Management Grid

From the Homescreen, click the **Project Management** tile. You land on the Project Management Grid — your repository of all visible projects.

	Name	
<input type="checkbox"/>	XU   GLO   ROLLOUT   DWE-COM CONTACT CENTER: ICCC Wave 4	<a href="#">P</a>
<input type="checkbox"/>	GY EV   GER   Impl.   GYMS 0043 Lauffen	<a href="#">P</a>
<input type="checkbox"/>	GLO EV   OneCRM   SFX   Release Q3/26	<a href="#">P</a>
<input type="checkbox"/>	XU   GLO   ROLLOUT   DWE-CLB M365 & POWER PLATFORM GOVERNANCE	<a href="#">P</a>
<input type="checkbox"/>	Mining Island – Secure Data Platform & Migration	<a href="#">P</a>
<input type="checkbox"/>	XU   EU   Legal   Interim Implementation for PPWR Support	<a href="#">P</a>
<input type="checkbox"/>	KI EV   FRA   Implementation   GYMS Lannemezan (LNZ) 4232	<a href="#">P</a>
<input type="checkbox"/>	XU   GLO   CIS   Cyber Defense Transformation – Year 3	<a href="#">P</a>
<input type="checkbox"/>	INT   IAM   GLO   MA I   2026	
<input type="checkbox"/>	XU   DE   Roll-Out   E-Invoice Germany Outbound	<a href="#">P</a>
<input type="checkbox"/>	XU   GLO   P4K   Release 2026.1	<a href="#">P</a>
<input type="checkbox"/>	IT   GLO   RELEASE   IT4IT ServiceNow 2026	<a href="#">P</a>
<input type="checkbox"/>	XU EV   GLO   ICCC   Rollout Wave 3 - Cluster 4	<a href="#">P</a>
<input type="checkbox"/>	GY   DE   Ortec Routing & Dispatch (ORD) Migration to SaaS	<a href="#">P</a>
<input type="checkbox"/>	GY   GLO   GDP   Foundations   Ignition Enterprise	<a href="#">P</a>
<input type="checkbox"/>	123Marc	
<input type="checkbox"/>	Service CRM	
<input type="checkbox"/>	CRM Service	
<input type="checkbox"/>	Service CPQ	
<input type="checkbox"/>	Service Procurement - PTP	
<input type="checkbox"/>	Service Procurement - STC	

10.11 2026 ProSymmetry LLC. All rights reserved.

**At a glance**

- **Toolbar** — + Add projects (chapter 4), Search, Filter, Insert columns, Group by, **View** selector.
- **Body** — one row per project, with the columns of the currently selected view.
- **Row actions** — hover a row to reveal the ⋮ **More** menu (Open, Clone, Delete-if-empty).

**View Management**

A **View** is the saved combination of: selected columns, applied filters, group-by setting and sort order. Knauf ships a small set of public views; PM/SM can clone them into personal views.

View type	Icon	Editable by you	Typical use
Public view	Blue eye	No — read-only	"All Active Projects", "My Department — Standard", PMO master views
Public default	Star (filled)	No	The view you land on when you open the grid
Personal view	Pencil / private	Yes	Your personal filter, e.g. "My projects, this quarter only"
Personal default	Star (outline)	You set it	One personal view auto-loads on grid open

**How to**

1. Open the **View** drop-down (top-right of the grid toolbar).
2. To save your current filter + columns: **Save as new view** → name it → choose *Private*.
3. To start from a public view: **Clone** the public view → adjust → save as private.
4. To set a personal default: open your view → click the star icon next to its name in the drop-down.

**Tip:** Don't fight the public views — clone them. Public views are versioned by the PMO and updated globally; your personal clones are immune from those updates.

## Search, Filter and Quick Filters

Control	Behaviour
Search bar	Searches the <i>Project name</i> column with <b>contains</b> logic
Filter	Adds column-level filters; multiple filters are AND-combined
Quick Filters	Predefined buttons in the toolbar — <i>My projects</i> , <i>Active</i> , <i>This quarter</i> , <i>Owner = me</i> , <i>Recently changed</i>
Group by	Group by any attribute; multi-level grouping supported (e.g. Phase → Owner)

**Note:** *My projects* uses the **owner** attribute on Attributes (chapter 5). If a project is missing from your *My projects* view, check the owner field first — it is almost always wrong-attribution, not a Tempus bug.

## Open a project

Two ways to open a project from the grid:

Action	Lands on	Use when
Click the <b>project name</b> (left-most column)	Attributes page	You want to start with master data
Hover the row → ⋮ <b>More</b> → pick <i>Allocations</i> / <i>Financials</i> / <i>Schedule</i> / ...	The chosen tab	You know exactly which tab you need

## Advanced tooltip — direct deep-link

Hovering over any project name shows an **Advanced Tooltip** with shortcut icons to all areas of that project that you have access to (Attributes, Allocations, Audit Log, Build Team, File Management, Financials, Milestones, Project Risk Profile, Schedule, Sheets, Snapshots).

### How to

1. Hover the project name in the grid — the Advanced Tooltip opens.
2. Click the area icon you want (e.g. **Financials**).



3. Tempus opens the project directly on that tab, skipping the default Attributes landing page.

**Tip:** Bookmark the project URL after you've opened it once — Tempus URLs are deep-linkable to the exact tab (Attributes / Allocations / Financials / ...). Pin a few high-traffic projects in your browser bookmarks for one-click access.

## Edit loop — same as Create

Once a project is open, the edit-loop is identical to the Create-time setup:

If you are editing...	Go to	Edit-loop reference
Master data (owner, dates, status, classification, custom flags)	<b>Attributes</b>	Chapter 5
Resources (named, generic, manday, cost view)	<b>Allocations</b>	Chapter 6
Financials (Cost Plan overrides, Budget vs. Actual, Re-forecast)	<b>Financials</b>	Chapter 7

The Check-out / Save / Check-in discipline applies on every page — see the warnings at the end of chapter 5 (Attributes) and chapter 6 (Allocations).

**Warning:** Editing **without check-in** is the #1 source of "ghost changes" at Knauf — the edits live on your machine but never reach Reports. Always check in before you sign off, even if it's "just a quick fix".

# Appendix

PM/SM

Blended PM/SM + PPM

## A. Keyboard Shortcuts

Tempus uses a small set of Excel-like shortcuts. The ones PM/SM use most:

Shortcut	Where it works	Action
Ctrl + C / Ctrl + V	Any grid	Copy / paste cell content
Tab	Editable grids	Move to next cell on the right
Enter	Editable grids	Move down one row
Shift + Click	Grid headers / cells	Select a column / range
Drag the "+" handle (bottom-right of a selected cell)	Editable grids	Replicate value across the dragged range
Ctrl + S	Anywhere	Save current page (equivalent to clicking Save)
Ctrl + F	Grids	Open the in-grid search
Esc	Modals	Close without saving

## B. Tempus Icon Reference (most used)

Icon	Meaning
Trash can	Delete selected item
Pencil	Edit / view selected item
Copy / Clone	Duplicate selected item
Lock / Unlock (open / closed padlock)	Whether record is locked by another user
Excel / CSV / PDF	Export the current view
Filter funnel	Apply column-level filter
Bell	Notifications — red dot = unread
Blue eye	Public (read-only) view

Star (filled)

Default view

Demand-resource silhouette

Generic / role-based resource row

Proposal marker

Resource on a project in *Planning* status

## C. Status Pills

Pill	Where	Meaning
<b>Available</b> (green)	Project header	Page is not checked out — anyone can edit
<b>Checked out by you</b> (yellow)	Project header	You hold the lock
<b>Checked out by &lt;name&gt;</b> (yellow w/ avatar)	Project header	Someone else is editing — read-only for you
<b>Planned / Baselined</b>	SPA grid header	Project's allocation has a baselined version
<b>Draft / Active / On Hold / Closed</b>	Attributes header	Project status (see chapter 5 status flow)

## D. What PM/SM Cannot See or Edit (Phase 1)

A quick lookup of fields and pages that are intentionally hidden or read-only for PM/SM in the Knauf Phase 1 rollout. Owners listed are the right contact when something needs to change.

Restricted item	Owner
Resource Rate Card overrides (per-resource)	RM / Finance
Resource Manager assignment per role	RM
Bulk Project Allocation Flatgrid	RM (separate guide)
Resource Replace (per project & advanced)	RM
Rate Card values (Hourly + Advanced)	Finance admin
Effective-date bands on the Rate Card	Finance admin
Currency configuration per project	PPM admin
Lock-period schedule	Finance admin
Actuals correction (timesheet adjustment)	Time-tracking admin

Custom attribute schema changes	Admin / PPM
Audit-log purge	Admin

## E. FAQ

**Q: I saved an attribute change but it's not visible in the report.** A: You probably forgot to **Check-in**. Save persists the value to your draft; Check-in releases the lock and triggers downstream visibility. Open the project → click *Check-in* → wait for the green toast → refresh the report.

**Q: The Cost shown in the Allocation grid (Cost view) is different from the Cost Plan on the Financials page.** A: You very likely have a **manual override** on the Financials page that does not match the calculated hours × rate. Open Financials → look for orange-dot cells in the Cost Plan panel → either right-click → *Reset to calculated*, or update the Allocation grid to match.

**Q: I want to delete a project I just created.** A: PM/SM can delete a project only as long as it has **no assignments and no actuals**. Open the grid → hover the row → *⋮ More* → *Delete*. If Delete is greyed out, the project already has data — contact PMO for archival instead.

**Q: A resource shows red in the Heatmap — is that a Tempus error?** A: No — the resource is over-allocated across all their projects (not just yours). Toggle to *Resource Heatmap* in Options to see the global picture; you typically need to discuss the conflict with the RM rather than change your plan unilaterally.

*\*Q: Why is my project missing from the My projects Quick Filter?* A: The My projects filter uses the Project owner attribute. If you are not the owner — even if you are doing the planning — the project will not show up. Either ask the current owner to change it, or use Owner = me\* via a custom filter.

**Q: How do I revert a wrong save?** A: Tempus does not have a global Undo. Two options: (1) Manually re-enter the previous value (you can see prior values in the Audit pane on the right of every project page) or (2) for SPA grid changes, ask an admin to restore the most recent baseline.

## F. Glossary

Term	Meaning
Allocation	Planned demand of a resource on a project for a given period
Actual	Logged hours from the timesheet system, multiplied by the applicable rate to give Actual cost
Assignment	The link between a resource and a project (one row in the SPA grid)

<b>Baseline</b>	A frozen snapshot of the plan, used as the comparison point for variance
<b>Blended (Knauf role)</b>	PM/SM + PPM combination — full Planner scope plus Portfolio view
<b>Check-out / Check-in</b>	Lock / release mechanism that allows safe editing
<b>Cost Plan</b>	Hours × applicable rate, shown on the Financials page
<b>Demand / Generic resource</b>	A role-based placeholder ("Senior Dev DE") that triggers a Resource Request
<b>Effective Rate</b>	The rate Tempus actually used for a given resource × month (Hourly or Advanced)
<b>Lock Period</b>	A closed financial period — Cost cannot be changed (soft or hard)
<b>Re-forecast</b>	Quarterly update of the Cost Plan for remaining open quarters
<b>Resource Request</b>	RM workflow that approves a demand on a resource
<b>SPA grid</b>	Single Project Allocation grid — the per-project planning surface
<b>Time grain / Time granularity</b>	The bucket size on the grid (Month, Quarter, Year)
<b>View</b>	Saved combination of filters, columns, group-by and sort
